

**STATUS OF PROJECTS IN EXECUTION – FY09
SOPE**

**EUROPE AND CENTRAL ASIA REGION
COUNTRY: TURKEY**

**Operations Policy and Country Services
OCTOBER 02, 2009**



Introduction

The Status of Projects in Execution (SOPE) Report for FY09 provides information on all IBRD/IDA projects that were active as of June 30, 2009. The World Bank has issued a SOPE Report every year as an internal communication to the Board of Executive Directors. In accordance with the Bank's revised disclosure policy, since FY02, the SOPE Report is available to the public.

The report is intended to bridge the gap in information available to the public between the Project Appraisal Document or Program Document, disclosed after the Bank approves a project, and the Implementation Completion Report, disclosed after the project closes.

In addition to the project progress description, the FY09 SOPE report¹ contains project level comparisons of disbursement estimates and actual disbursements, and a table showing the loan/credit/grant amount and disbursements to date.

¹ Notes:

- Amounts and Graphs for loans/credits/grants in currencies other than U.S. dollars may not match exactly due to exchange rate fluctuations over the life of the project.
- Disbursement graphs are not included for Development Policy Operations, which provide quick-disbursing financing to support policy and institutional reforms. For these operations, funds are disbursed in one or more stages (tranches), released when the borrower complies with agreed prior actions.
- Projects which are not yet effective may not have a planned disbursement schedule and thus will not include a graph.



Turkey


Project Name(ID):	PSSP 2 (P094167)
Country:	Turkey
Board Approval Date:	14-Jun-2005
Mid-Term Review Date:	
Closing Date:	31-Oct-2009
Sector:	Compulsory pension and unemployment insurance (94%); Central government administration (3%); Other social services (1%); General industry and trade sector (1%); General education sector (1%)
The project was restructured, or received Additional Financing during FY09:	no
Project development objective(s):	<p>The project's objective is to support Turkey's privatization program through mitigating the negative social and economic impact of the privatization of state-owned enterprises.</p> <p>The project has supported the provision of temporary incomes support (job loss compensation) to more than 12,000 workers affected by State Owned Enterprises. Additionally, 8,546 workers benefitted from labor redeployment services, including on-the-job-training and temporary community employment, to assist them in re-entering the labor market. The average job placement rate has been 64 percent. Five incubators have also been supported under the project, in addition to the six already established under the first Privatization Social Support operation. Most of the project's activities have been completed as of end-June 2009, with only a small portion of the operation remaining active until the end of October, 2009.</p>
Progress toward achieving development objective(s):	

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47910	Effective	EUR	503.69	404.42	58.32	20.88



Lending Information/Disbursement Summary (in millions USD)

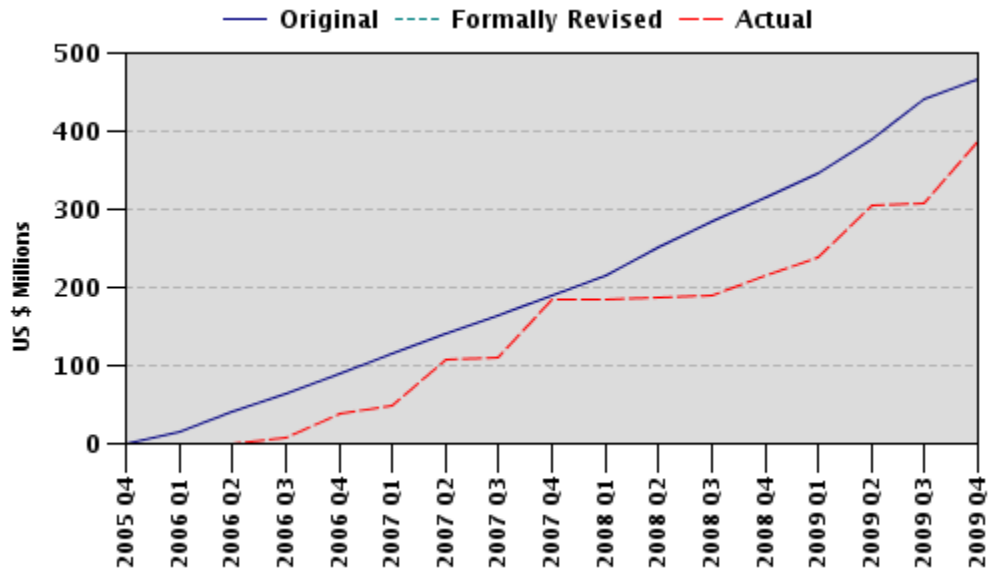

Project Name(ID): ECSEE APL 2 (TURKEY) (CRL) (P094176)
Country: Turkey
Board Approval Date: 04-Apr-2005
Mid-Term Review Date: 26-Jan-2008
Closing Date: 31-Dec-2010
Sector: Power (100%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s):

The project supports the implementation of investments by Turkish Electric Transmission Corporation (TEIAS) including the market management system, strengthening of control systems, and grid strengthening.


Progress toward achieving development objective(s):

The project is nearing completion. The market management system is being phased in gradually--Turkey's market is already quite large and liquid with about 20 percent of electricity consumption being transacted through the market. System controls have been improved through upgrades and expansions, to provide better system reliability.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47720	Effective	EUR	71.26	35.70	34.82	0.00

Lending Information/Disbursement Summary (in millions USD)

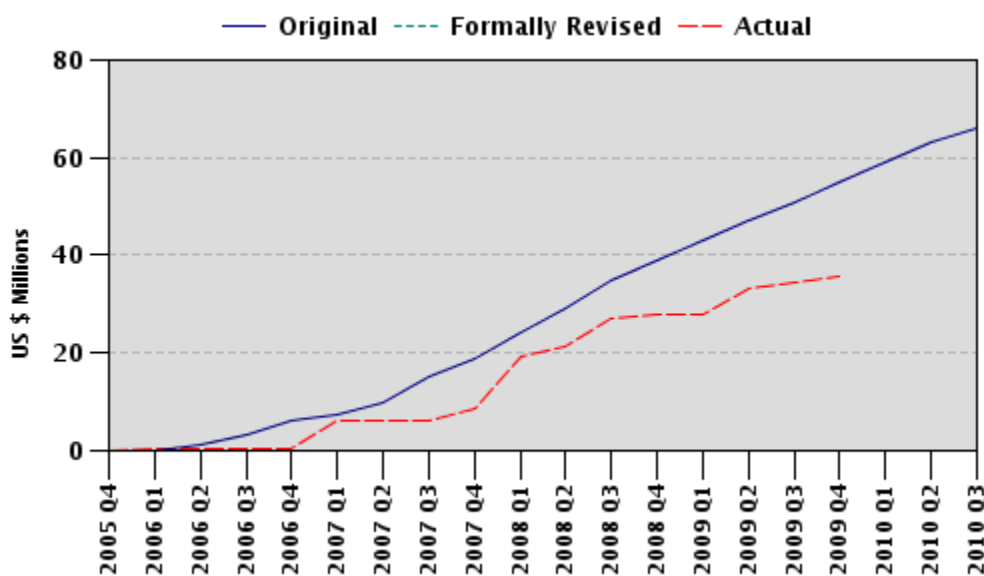


Project Name(ID): SEISMIC RISK MITIGATION (P078359)
Country: Turkey
Board Approval Date: 26-May-2005
Mid-Term Review Date: 10-Oct-2008
Closing Date: 30-Sep-2010
Sector: Sub-national government administration (40%); Other social services (20%); Health (20%); General education sector (20%)
The project was restructured, or received Additional Financing during FY09: no
Project development objective(s): The development objective of the project is to improve the city of Istanbul's preparedness for a potential earthquake.
The project is progressing well towards achieving its development objective. To date, some 370 public facilities, predominantly schools and hospitals, have been retrofitted or rebuilt. The state-of-the-art Governorship Disaster Management Center was established in Istanbul and equipped with modern information and communication technologies. The project has been helping enhance institutional capacities of emergency response agencies with provision of equipment for first responders. Two pilot Istanbul municipalities are assisted in establishment of IT systems for better land use planning and building permit issuance, and were provided with training in land use planning in disaster prone areas.
Progress toward achieving development objective(s):

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47840	Effective	EUR	439.97	213.44	227.74	0.00
TF-52686	Closed	USD	0.93	0.82	0.00	0.11



Lending Information/Disbursement Summary (in millions USD)

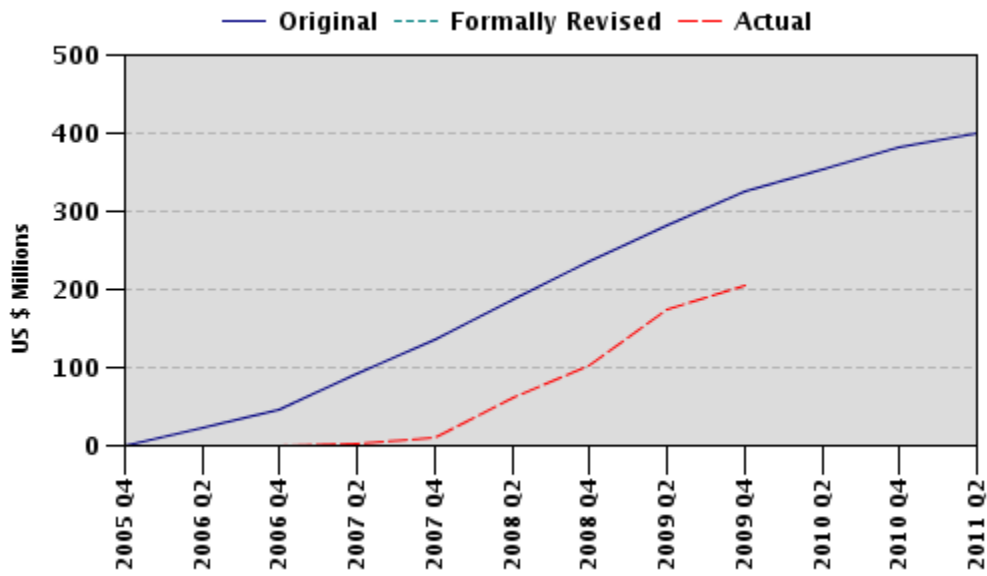

Project Name(ID): Private Sector RE and EE Project (P112578)
Country: Turkey
Board Approval Date: 28-May-2009
Mid-Term Review Date:
Closing Date: 31-Dec-2014
Sector: Renewable energy (90%); District heating and energy efficiency services (10%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project will finance renewable and energy efficiency investments, in order to help improve supply security as well as the energy sector's environmental sustainability.

Progress toward achieving development objective(s): The project loan was not effective by the close of the reporting period. The project is the first to use financing from the newly launched Clean Technology Fund. Potential projects are currently being assessed by the two Turkish banks involved in the project.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-77140	Not Effective	USD	150.00	0.00	150.00	0.00
IBRD-77150	Not Effective	USD	350.00	0.00	350.00	0.00
TF-94498	Not Effective	USD	70.00	0.00	70.00	0.00
TF-94499	Not Effective	USD	30.00	0.00	30.00	0.00



Project Name(ID): ANATOLIA WATERSHED REHAB (P070950)
Country: Turkey
Board Approval Date: 01-Jun-2004
Mid-Term Review Date: 29-May-2008
Closing Date: 30-Jun-2012
Sector: General agriculture, fishing and forestry sector (50%); General water, sanitation and flood protection sector (15%); Agro-industry (13%); Irrigation and drainage (13%); Central government administration (9%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project's overall development objective is to support sustainable natural resource management practices in 28 microcatchments in Anatolia and Turkey's Black Sea Region and, thereby, raise incomes of communities affected by resource degradation.


Progress toward achieving development objective(s): Project activities are being implemented as outlined in participatory microcatchment management plans, which are prepared by closely involving villages in identifying key natural resource degradation processes and jointly agreeing on project-financed solutions to these. Twenty-four microcatchment plans (out of 28 planned) have been completed and are under implementation, and another four microcatchments are in the process of being identified for implementation support next calendar year. Implementation delays which have occurred are not out of the ordinary, and are generally being overcome where they occur. The project is also providing support for building on the framework for agricultural pollution control outlined in the European Union Nitrates Directive and is consistent with the objectives of the Black Sea Strategic Partnership Nutrient Reduction Investment Program. As such, the project continues to contribute to the European Union Accession framework.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47410	Effective	USD	20.00	11.41	4.29	4.30
IBRD-P3970	Closed	USD	0.28	0.01	0.00	0.27



Lending Information/Disbursement Summary (in millions USD)

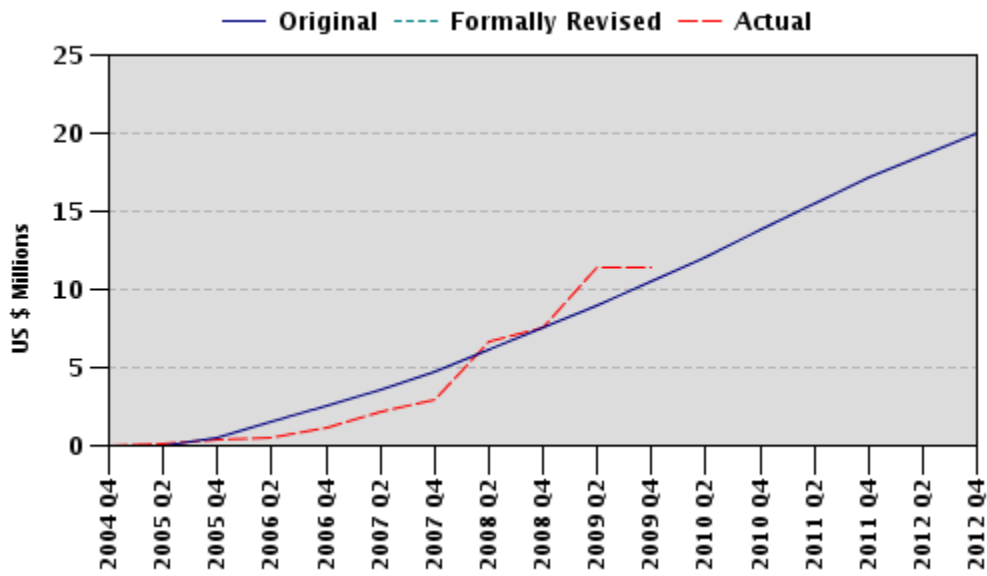

Project Name(ID): Land Regis & Cadastre Modernization Proj (P106284)
Country: Turkey
Board Approval Date: 01-May-2008
Mid-Term Review Date:
Closing Date: 30-Sep-2013
Sector: Central government administration (98%); Sub-national government administration (2%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The objective of the project is to improve the effectiveness and efficiency of the land registry and cadastre services.
Progress has started; however, steps have been taken to initiate work which would reconfirm measurements of about 167,000 parcels and an area of 2.4 million hectares. Design of a prototype modern building focused on delivery of cadastre services will also start in the fall of 2009. The completed human development strategy will improve the effectiveness of the staff of the cadastre and registration agency in delivering services.

Progress toward achieving development objective(s):

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-75370	Effective	USD	203.00	0.00	203.00	0.00



Project Name(ID): ECSEE APL 3 (TURKEY) (P096400)

Country: Turkey

Board Approval Date: 24-Mar-2006

Mid-Term Review Date:

Closing Date: 30-Jun-2011

Sector: Power (100%)

The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The project aims to help increase the safety, reliability and capacity of the transmission system.

Progress toward achieving development objective(s): In the main load center of Istanbul, system capacity and reliability have increased, helping provide better quality of electricity supply in the area.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-48170	Effective	EUR	175.83	133.83	41.89	0.00

Lending Information/Disbursement Summary (in millions USD)

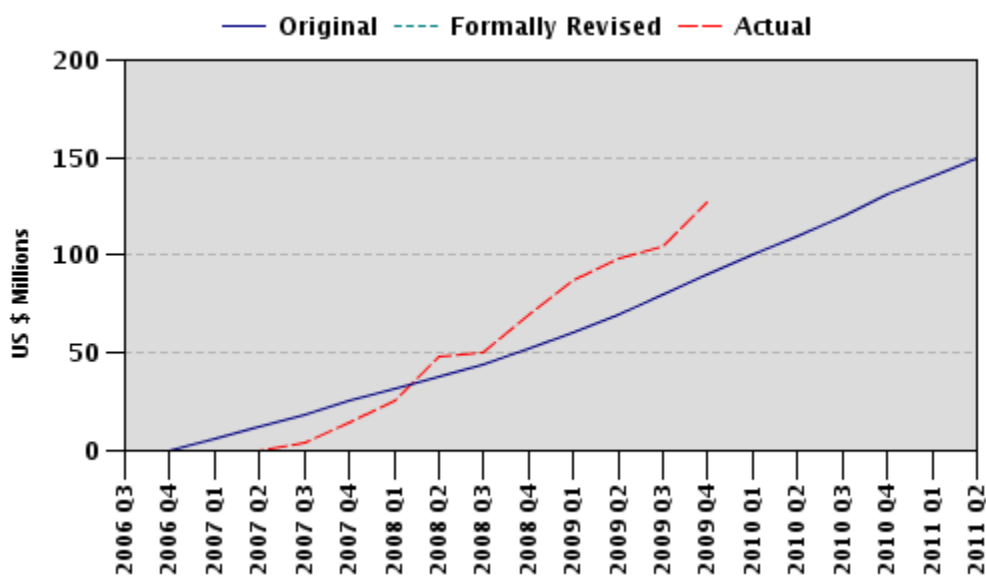

Project Name(ID): ELECT DISTRIB REHAB (P096801)
Country: Turkey
Board Approval Date: 19-Apr-2007
Mid-Term Review Date:
Closing Date: 31-Dec-2012
Sector: Power (100%)

The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The project aims to help improve reliability of power supply to consumers in Turkey through the rehabilitation and expansion of the electricity distribution system.

Progress toward achieving development objective(s): The project will cover eight to nine provinces across the country, and currently the distribution grid in seven cities is being rehabilitated.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-48580	Effective	EUR	286.59	14.28	272.59	0.00

Lending Information/Disbursement Summary (in millions USD)

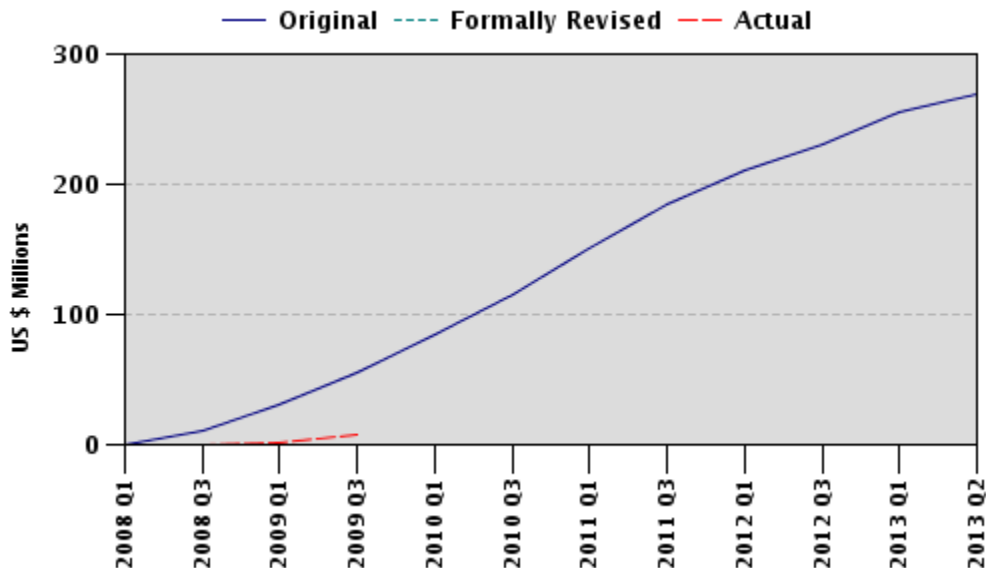

Project Name(ID): EFIL IV (P096858)
Country: Turkey
Board Approval Date: 22-May-2008
Mid-Term Review Date:
Closing Date: 30-Jun-2013
Sector: General industry and trade sector (50%); General finance sector (20%); Banking (15%); Micro- and SME finance (15%)

The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The objectives are to provide medium and long-term finance to exporters to facilitate export growth and improve the quality, the safety of, and access to finance.

Progress toward achieving development objective(s): Provision of medium-term finance to exporters in Turkey has progressed well. Exporters' investments and working capital have been supported in an amount of US\$149 million equivalent as of June 30th. The funds have been intermediated by the two borrowers, five additional banks, and five leasing companies.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-75380	Effective	USD	300.00	192.59	101.32	0.00
IBRD-75390	Effective	USD	300.00	31.51	267.40	0.00

Lending Information/Disbursement Summary (in millions USD)

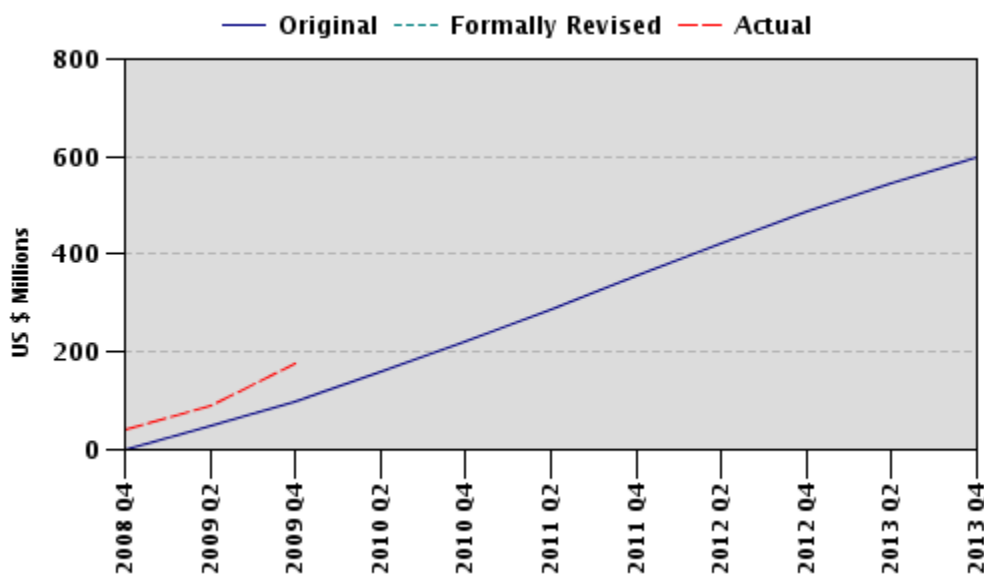

Project Name(ID): RENEW ENERGY (P072480)
Country: Turkey
Board Approval Date: 25-Mar-2004
Mid-Term Review Date: 14-Jan-2008
Closing Date: 30-Jun-2010
Sector: Renewable energy (50%); Micro- and SME finance (40%);
 Central government administration (10%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s):

The objective is to increase privately owned and operated distributed power generation from renewable sources, without the need for government guarantees, within the market-based framework of the new Turkish Electricity Market Law.

Progress toward achieving development objective(s):


The project has surpassed its development objective targets. Capacity increased by about 575 megawatts. Additional generation is about 2377 gigawatts. Annual carbon emission reductions are about 1 million tons of carbon dioxide. The project has helped create a sustainable market for financing private renewable energy projects, and its successes have encouraged other financiers to enter the market. The project has thus far helped finance about half of the total Turkish renewable energy capacity.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-72210	Effective	USD	202.03	201.01	0.00	1.02
TF-51629	Closed	USD	0.48	0.43	0.00	0.05



Lending Information/Disbursement Summary (in millions USD)

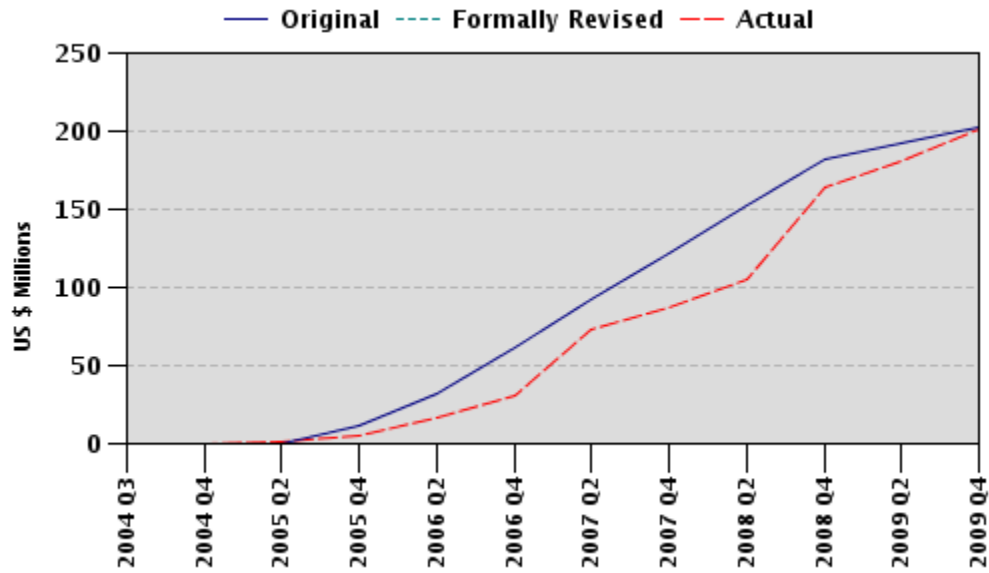

Project Name(ID): Programmatic Electricity Sector DPL (P110643)
Country: Turkey
Board Approval Date: 11-Jun-2009
Mid-Term Review Date:
Closing Date: 31-Dec-2009
Sector: Power (80%); District heating and energy efficiency services (10%); Central government administration (10%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project supports the implementation of the Government of Turkey's program to address the projected electricity supply-demand imbalance through energy efficiency measures to reduce the rate of growth of demand for electricity, and by enhancing the efficient supply of electricity.

Progress toward achieving development objective(s): Key policy actions under this program over the last year include the following: approval of an updated national electricity strategy, amendments of the Electricity Market Law to ensure security of electricity supply, issuance by the Energy Market Regulatory Authority of regulations to improve the functioning of the wholesale market, a decision to provide the necessary budgetary allocations in line with approved transmission system investment plans to achieve efficient and reliable transmission of the increasing amount of electricity supply, issuance of secondary regulations related to energy efficiency, launch of a national energy efficiency campaign to use energy efficiently and effectively, revision of retail electricity prices to offset the impact of cost increases and approval of a cost-based pricing mechanism that automatically covers future increases in costs incurred by the electricity sector state owned enterprises. The first adjustment of tariffs under this mechanism was implemented with effect from October 1, 2008. Privatization of four distribution companies has been completed.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-77180	Effective	USD	800.00	773.79	0.00	0.00



Project Name(ID): ISTANBUL MUNICIPAL INFRASTRUCTURE PROJ. (P100383)
Country: Turkey
Board Approval Date: 28-Jun-2007
Mid-Term Review Date:
Closing Date: 31-Dec-2011
Sector: Solid waste management (30%); General transportation sector (23%); Sub-national government administration (23%); General water, sanitation and flood protection sector (13%); Housing construction (11%)
The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The project development objectives are to assist the Istanbul Metropolitan Municipality in: improving its solid waste management and improving its capacity to mitigate earthquakes by retrofitting key facilities and infrastructure and upgrading the institutions and their procedures to help them respond to emergencies.

Progress toward achieving development objective(s): The project loan became effective in the latter part of the reporting period and was still in too early a stage for meaningful progress.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-48660	Effective	USD	322.15	0.81	321.34	0.00

Lending Information/Disbursement Summary (in millions USD)

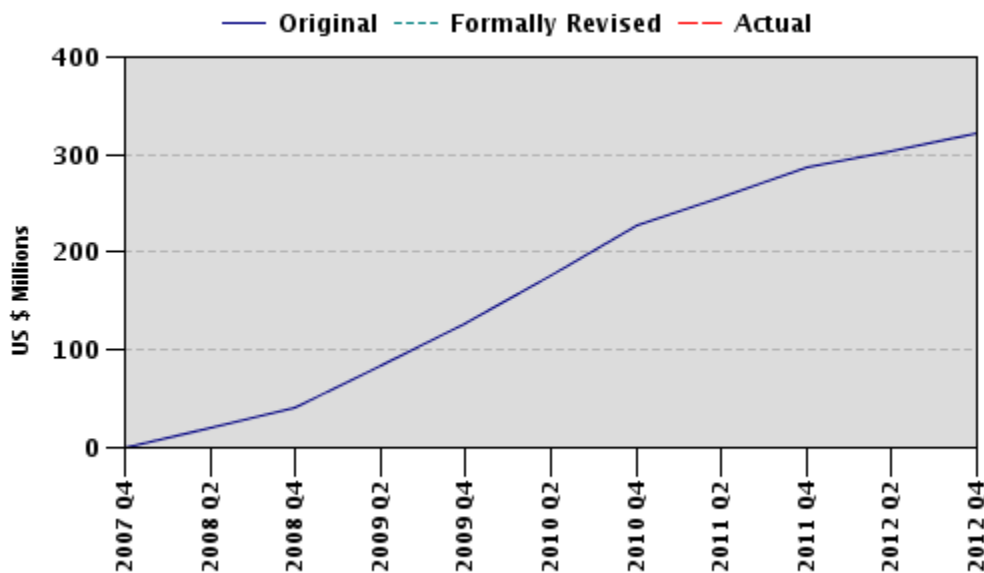

Project Name(ID): HEALTH TRANSIT (APL 1) (P074053)
Country: Turkey
Board Approval Date: 20-May-2004
Mid-Term Review Date: 04-Sep-2006
Closing Date: 31-Dec-2009
Sector: Central government administration (60%); Health (30%);
 Compulsory health finance (10%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project objective is to: (a) help expand the capacity of the Ministry of Health and the Social Security Institute to formulate and effectively implement health policies, health sector regulatory mechanisms, and health insurance functions; and (b) support the implementation of critical health services delivery reforms (family medicine and hospital autonomy) with the objective of improving access, efficiency, quality and fiscal sustainability of the health sector.


Progress toward achieving development objective(s): Out of eight project development objectives, six are already achieved, and one will be achieved by project closing. The Ministry of Labor and Social Services is no longer a provider of health services. Ninety percent of the population is enrolled with family doctors in at least 15 provinces of the country. Enrollment rates are high (over 90 percent), and the number of primary care visits have increased while referral rates have decreased in pilot provinces as compared with non-pilot provinces, health insurance coverage has increased among vulnerable groups. Performance has improved (in quality and efficiency) in at least 50 percent of Ministry of Health hospitals as compared with the baseline. Contracts based on prospective payments systems have been implemented between the Universal Health Insurance fund and at least 20 percent of public hospitals and all private hospitals. The indicator on adoption of a human resources strategy is expected to be achieved before project closing. The indicator on hospital autonomy will not be achieved since these reforms will now be implemented under the new health project.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47370	Effective	EUR	69.49	42.52	13.64	12.22
TF-51884	Closed	USD	0.80	0.46	0.00	0.34



Lending Information/Disbursement Summary (in millions USD)

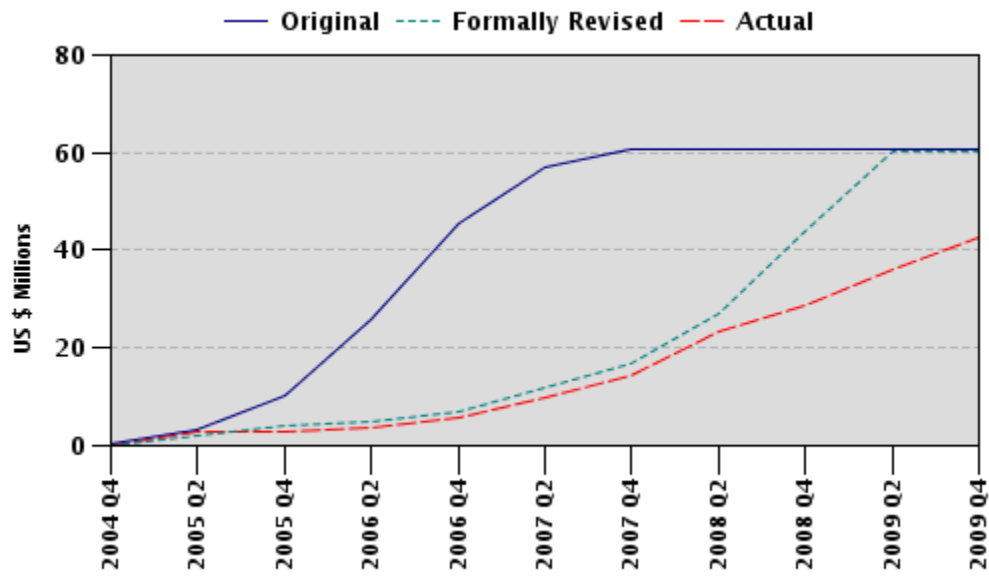


Project Name(ID): ACC TO FIN FOR SMEs (P082822)
Country: Turkey
Board Approval Date: 08-Jun-2006
Mid-Term Review Date:
Closing Date: 30-Apr-2012
Sector: Micro- and SME finance (70%); General finance sector (15%); General industry and trade sector (10%); Banking (5%)
The project was restructured, or received Additional Financing during FY09: Additional financing of US\$ 200 million equivalent was provided to Halkbank for lending to small and medium enterprises to enable further expansion of the sectors covered and
Project development objective(s): The objective is to increase small and medium-sized enterprises' access to medium-term finance.
The progress has been substantial. Out of the original 200 million Euro project, 186 loans for small- and medium-sized enterprises throughout the 40 provinces in the country totaling 160 million Euro have been made by Halkbank and Turkiye Sinai Kalkinma Bankasi. With the additional financing of this project, \$40 million is loans have been made by Halkbank for 35 small- and medium-sized enterprises. All loans are performing and have maturities of at least one year. These loans have resulted in direct job creation of over 3,200 jobs.
Progress toward achieving development objective(s):

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-73890	Effective	USD	60.07	70.59	0.00	0.00
IBRD-73900	Effective	USD	120.14	100.31	30.04	0.00
IBRD-74620	Effective	USD	66.70	77.39	0.00	0.00
IBRD-76060	Effective	USD	200.00	151.24	56.35	0.00



Lending Information/Disbursement Summary (in millions USD)

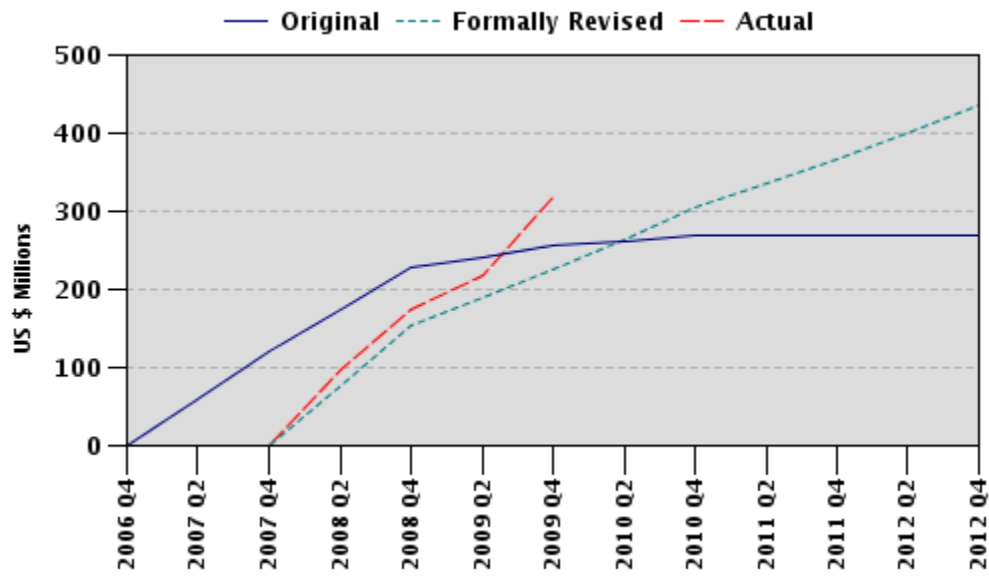

Project Name(ID): ELECTRICITY GENERATION REHAB & RESTRUCTU (P085561)
Country: Turkey
Board Approval Date: 06-Jun-2006
Mid-Term Review Date:
Closing Date: 31-Dec-2011
Sector: Power (100%)
The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The project will finance the rehabilitation of the largest lignite power plant in Turkey, with a view to improving energy security.

Progress toward achieving development objective(s): The project is delayed, mainly because of the complexity involved in this type of investment.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-48240	Effective	EUR	357.18	0.89	391.47	0.00
TF-53753	Closed	USD	0.60	0.54	0.00	0.06

Lending Information/Disbursement Summary (in millions USD)

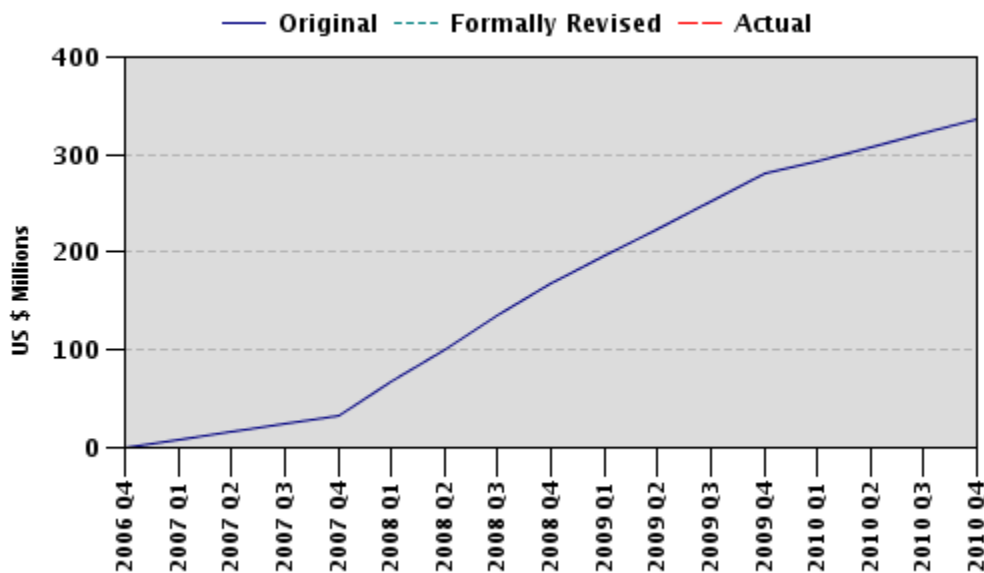

Project Name(ID): HEALTH & SOC. SECURITY REF (APL2) (P102172)
Country: Turkey
Board Approval Date: 11-Jun-2009
Mid-Term Review Date:
Closing Date: 31-Jul-2013
Sector: Public administration- Health (78%); Health (17%);
 Compulsory health finance (5%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The specific objectives of the project are: (a) increasing the effectiveness of the Social Security Institute and the Ministry of Health in formulating and implementing reforms in provider payments and health systems performance; and (b) piloting output-based financing for non-communicable diseases prevention and control.

Progress toward achieving development objective(s): The project was not effective before the close of the reporting period.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-77170	Not Effective	USD	75.13	0.00	75.13	0.00
TF-90317	Closed	USD	0.88	0.68	0.20	0.00



Project Name(ID): RAIL RESTRUCT (P077328)
Country: Turkey
Board Approval Date: 09-Jun-2005
Mid-Term Review Date: 11-Nov-2008
Closing Date: 30-Jun-2012
Sector: Railways (100%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project's development objective is to improve the financial viability, productivity and effectiveness of railway operations.

Progress toward achieving development objective(s):


At the time covered by this report, the project was being restructured to adapt the project's objective to what can be achieved within the existing legal framework. The new objective is to improve railway service on the Mersin-Toprakkale and Yenice-Bogazköprü lines and lay the groundwork for restructuring the Turkish Railway. Preliminary work has started on the signaling investment that will improve service on the Mersin-Toprakkale and Yenice-Bogazköprü lines. When Turkish Railway is restructured to conform to the EU *acquis communautaire* on railways, it will need to execute public service obligation contracts and track access on a broad scale. Under the project the Turkish railway piloted studies on public service obligation contracts and track access to gain relevant experience.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47870	Effective	EUR	197.07	44.75	158.49	0.00
TF-53200	Closed	USD	0.70	0.70	0.00	0.00



Lending Information/Disbursement Summary (in millions USD)

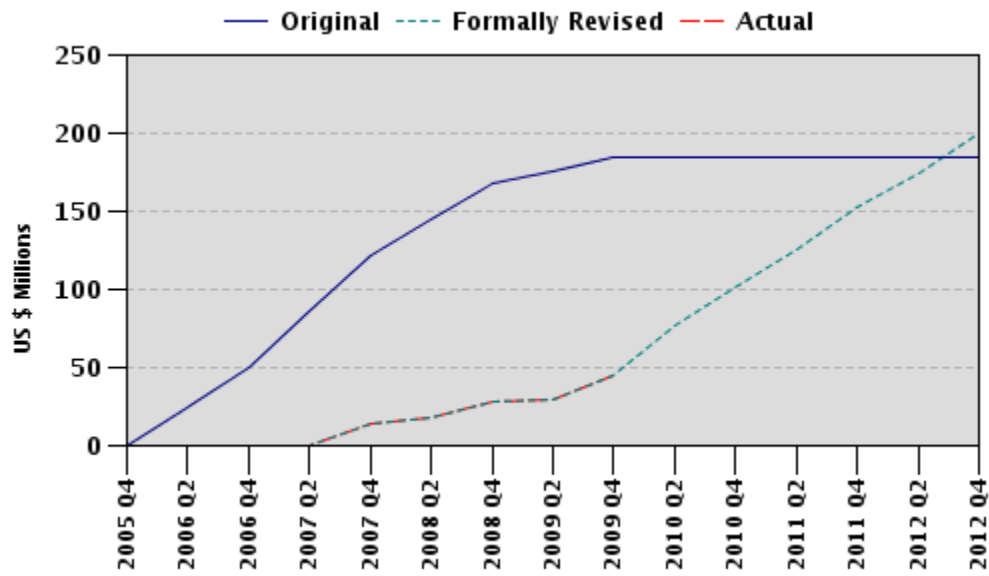

Project Name(ID): MUNICIPAL SERVICES (P081880)
Country: Turkey
Board Approval Date: 23-Jun-2005
Mid-Term Review Date:
Closing Date: 30-Jun-2010
Sector: Water supply (43%); Sewerage (33%); Solid waste management (16%); Sub-national government administration (8%)
The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The objective is to support municipal development in a sustainable manner. To this end, the project will: support the development of municipal infrastructure to provide quality local services and support the institutional strengthening of Iller Bank, which is the source of financing for municipalities.
 The project is meeting its development objectives by gradually improving municipal services and further assisting to strengthen the capacity of Iller Bank through the technical assistance component. The coordination and facilitation by Iller Bank with the municipalities and utilities is proceeding well and is a good example of the central and local levels working together, contributing to the project's institutional objectives through capacity building. The technical assistance component is proceeding extremely well. Training in financial and economic analysis has taken place to further strengthen the capacity of Iller Bank staff and the utilities and municipalities. The investments have assisted to expand municipal services to serve 3.3 million users, thereby exceeding at mid-term the Country Partnership Strategy's target of 2 million.


Progress toward achieving development objective(s):

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-73120	Effective	USD	275.00	94.01	189.53	0.00
TF-53127	Closed	USD	0.50	0.48	0.00	0.02



Lending Information/Disbursement Summary (in millions USD)

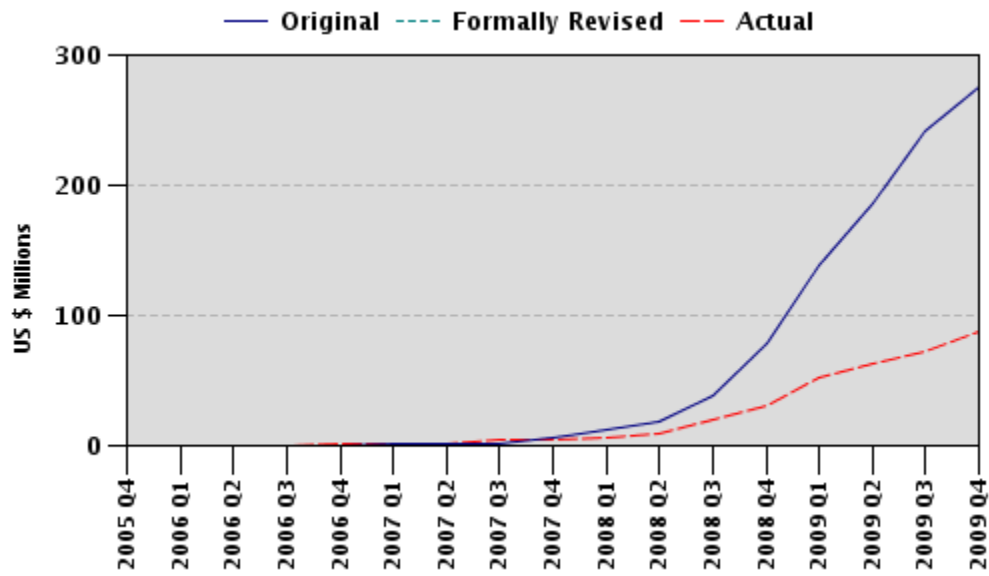

Project Name(ID): AVIAN FLU - TR (P096262)
Country: Turkey
Board Approval Date: 24-Apr-2006
Mid-Term Review Date: 17-Oct-2008
Closing Date: 30-Nov-2010
Sector: General public administration sector (45%); Health (28%);
 Agricultural extension and research (13%); Animal production
 (12%); Other social services (2%)

The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project aims to minimize the threat in Turkey posed to humans by the highly pathogenic avian influenza infection and other zoonoses in domestic poultry and prepare for the control and response to an influenza pandemic and other infectious disease emergencies in humans.


Progress toward achieving development objective(s): Progress toward meeting the development objectives has been good. For example the preparedness and knowledge on the part of the Ministry of Agriculture and Veterinary Services staff remains high; the Ministry of Health-Primary Health Care level of preparedness and knowledge for avian influenza outbreak and pandemic are also high. Monitoring and evaluation findings reveal useful information regarding effectiveness of training. Well-designed communications materials have been produced and distributed all over the country. All poultry-sector biosecurity improvement pilot projects, communications, training and technical assistance activities were completed. The Ministry of Health made a fast response to the Influenza A (H1N1), informed the public of the disease, and took measures against its possible spread. In addition the ministry successfully started public awareness activities on avian influenza and other human pandemic diseases.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-48220	Effective	EUR	38.85	13.38	24.95	0.00
TF-57375	Closed	USD	0.98	0.98	0.00	0.00



Lending Information/Disbursement Summary (in millions USD)

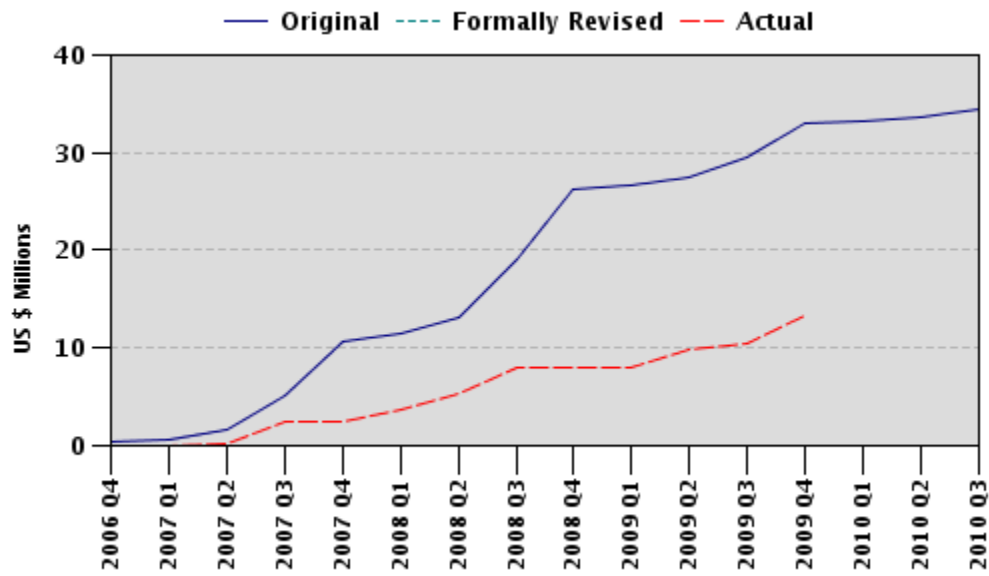

Project Name(ID): SEC EDUC (P066149)
Country: Turkey
Board Approval Date: 15-Mar-2005
Mid-Term Review Date:
Closing Date: 31-Dec-2010
Sector: Secondary education (50%); Vocational training (33%);
 Central government administration (17%)

The project was restructured, or received Additional Financing during FY09: no


Project development objective(s): The objective is to improve conditions for student learning, establish a career guidance system, and enhance foreign language teacher training.

Progress toward achieving development objective(s): Some parts of the project are implementing well, including activities related to revision of curricula, career guidance and counseling, and vocational training initiatives. Other areas, including foreign language teacher training, are delayed or are not implementing at all. As a result of the limited progress in implementation, there is no impact yet on project outcomes.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-47670	Effective	EUR	111.67	13.48	98.99	0.00
TF-26143	Closed	USD	0.29	0.03	0.00	0.26

Lending Information/Disbursement Summary (in millions USD)

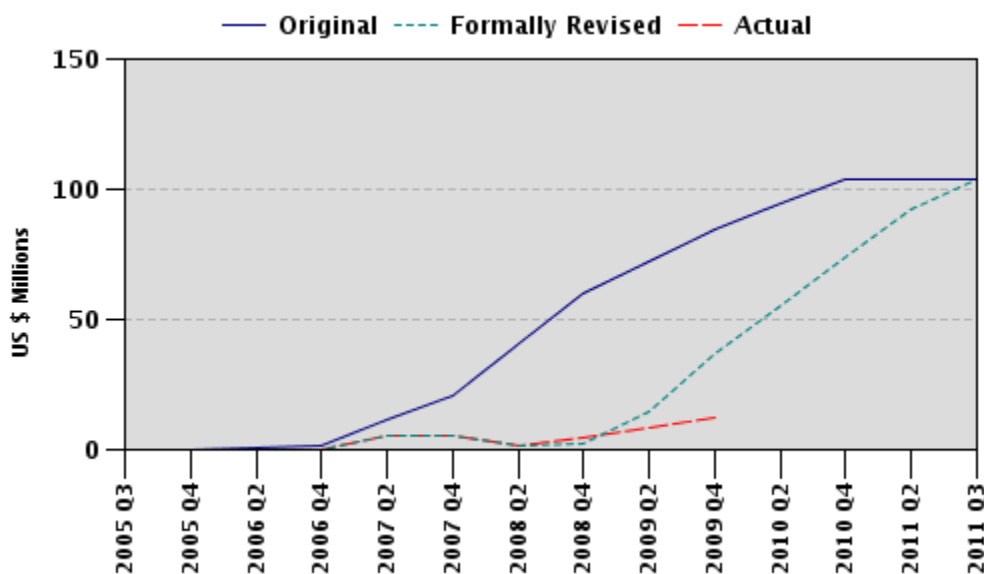

Project Name(ID): GAS SECT DEVT (P093765)
Country: Turkey
Board Approval Date: 29-Nov-2005
Mid-Term Review Date:
Closing Date: 31-Dec-2012
Sector: Oil and gas (100%)
The project was restructured, or received Additional Financing during FY09: no

Project development objective(s): The project aims to help increase gas supply reliability and security by financing gas storage and network infrastructure, and by supporting the commercial operations of the Turkish Pipeline Corporation.

Progress toward achieving development objective(s): The start of the project has been delayed by about two years and is expected to commence later in 2009.

Lending Information/Disbursement Summary (amounts in millions, as of Aug 17, 2009)

Loan/Credit/Grant	Status	Currency	Amount	Disbursed	UnDisbursed	Cancellation
IBRD-73420	Effective	USD	325.00	4.31	320.69	0.00

Lending Information/Disbursement Summary (in millions USD)

